




BUILDING GRADE FORM

GRADE SLIP NO.	0409-17-10
JOB NO.	112944505
SUBDIVISION	EASTSIDE PH 1
DEVELOPER	TOWN OF REDCLIFF
REVISION DATE	SEPT. 15, 2016


ADDRESS 935 - MASKEL PLACE SE		
LOT 17	BLOCK 10	REG'D PLAN NO. 091 3590

BUILDER	REPRESENTATIVE
ADDRESS	PHONE NO.

PROPOSED BUILDING GRADES

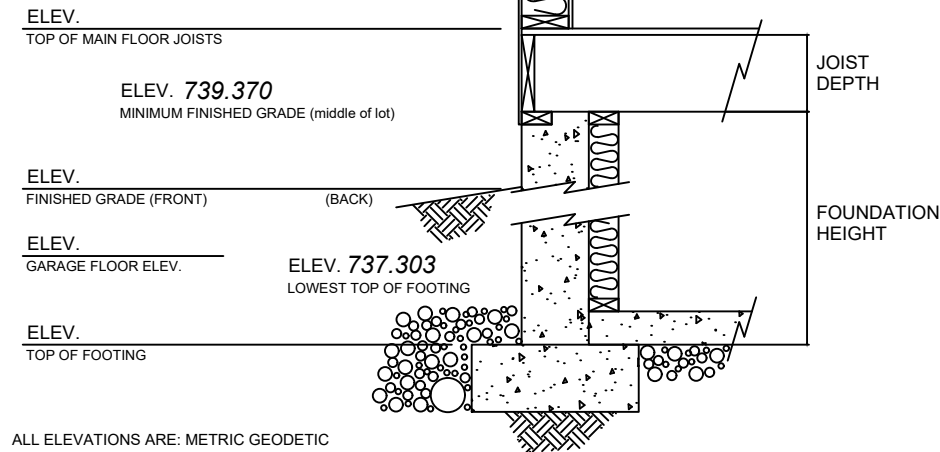

LEGEND

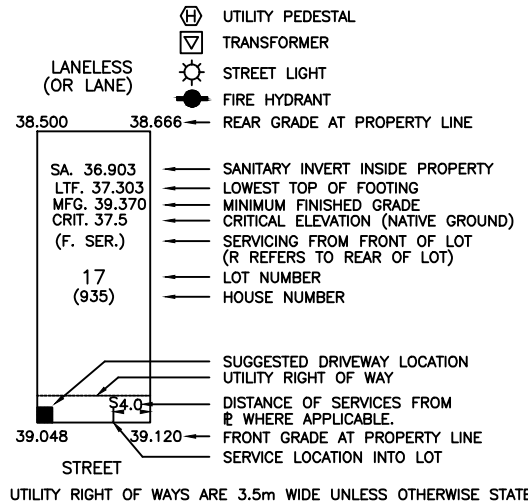


ADDITIONAL REQUIREMENTS

	FRONT	REAR	CENTERED	REFER TO PLAN	SIZE	TYPE
SANITARY	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	100mm	PVC
STORM (WTD)	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>		
WATER	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	25mm	PVC

- BUILDING SETBACKS 6m FRONT 6m BACK 1.5m SIDE
- GROUND WATER DRAIN WITH BACKFLOW PREVENTER TO SEWER REQUIRED (WTD) YES NO
- GROUND WATER DRAIN TO SUMP PUMP REQUIRED YES NO
- WATER PRESSURE REDUCING VALVE REQUIRED (PRV) YES NO
- SERVICE INSTALLED 3.50m INSIDE OF PROPERTY YES NO
- HIGH SULFATE CONCENTRATIONS PRESENT IN THE SOIL SULPHATE RESISTANT CEMENT (TYPE 50) REQUIRED YES NO
- ADDITIONAL SULPHATE REQUIREMENTS (SEE NOTE BELOW) YES NO
- FOUNDATION SOIL BEARING INVESTIGATION AND CERTIFICATION REQUIRED (SEE NOTE BELOW) YES NO
- GEOTECHNICAL RESTRICTIONS APPLY YES NO
- UTILITY EASEMENTS YES NO
- FOOTING ELEVATION CHECK REQUIRED PRIOR TO POURING (MAX. 100MM DEVIATION) (NOTIFY ENGINEER 48 HOURS IN ADVANCE - COST COVERED BY THE TOWN OF REDCLIFF) (ENGINEER - TOWN OF REDCLIFF PLANNING AND ENGINEERING (403)548-9263 Cell - (403)502-2854) YES NO
- MINIMUM GRADE CHECK REQUIRED PRIOR TO COMPLETION (MAX. 100MM DEVIATION) (NOTIFY ENGINEER 48 HOURS IN ADVANCE - COST COVERED BY THE TOWN OF REDCLIFF) (ENGINEER - TOWN OF REDCLIFF PLANNING AND ENGINEERING (403)548-9263 Cell - (403)502-2854) YES NO

- IT IS THE RESPONSIBILITY OF THE BUILDER TO ENSURE THE FOOTINGS ARE PLACED ON A PROPER BASE THAT IS FREE FROM FROST, EXCESSIVE MOISTURE AND DELETERIOUS MATERIALS AND HAVE APPROPRIATE FROST PROTECTION WHEN COMPLETE.
- LIST OTHER CONSTRAINTS BELOW.
- NOTES:
 - * COSTS OF ANY UNEXPECTED FILL MATERIAL ENCOUNTERED AFTER EXCAVATION IS COMPLETED INCLUDING ANY ADDITIONAL EXCAVATION OR DESIGN SHALL BE AT THE COST OF THE PROPERTY OWNER.
 - * IF PROPOSED FOOTING IS ABOVE CRITICAL ELEVATION (NATIVE GROUND) A FOUNDATION SOIL BEARING INVESTIGATION AND CERTIFICATION IS REQUIRED.

PLAN

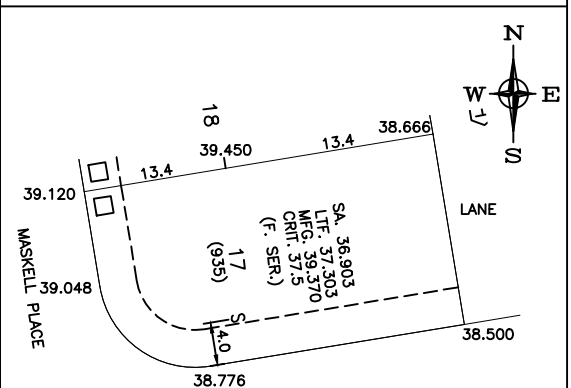

I CERTIFY THAT THE FINAL HOUSE PLANS PROVIDED, IN THE BUILDING PERMIT APPLICATION, ARE THE SAME AS PROCESSES UNDER THIS GRADE SLIP AND THAT I UNDERSTAND THE INFORMATION AND THE REQUIREMENTS CONTAINED HEREIN AND WILL BUILD ACCORDINGLY.

AUTHORIZED BUILDER'S REPRESENTATIVE _____

SIGNATURE _____ DATE _____

THE INFORMATION CONTAINED HEREIN IS BASED ON THE APPROVED BUILDING GRADE PLAN FOR THIS SUBDIVISION.

APPROVED BY AUTHORIZED TOWN REPRESENTATIVE _____

SIGNATURE _____ DATE _____
